

SDI Intelligence Programme Status

Three workstreams · one calendar · the loop closed

ISSUED 16 SEP 2026
SUPERSEDES 7 SEP 2026
OWNERS J. GRAY · Y. KUMAR · M. YAZIR
COMPILED BY J. GRAY

Status across **SDI Estimating Intelligence**, **SDI Technical Design Intelligence** and **SDI Creative Design Intelligence**, nine days on from the second combined report. The estimating engine has run **eleven jobs in two weeks** against the estimators' own sheets and, for the first time, **the feedback has come back from all three estimators** — Howard on two jobs, Tony on one, Tim on three — and every point has gone in as a rule that carries to every job. Six more run this week. Technical Design's second tool is being **hardened for 29 September** and the PDM environment is up. **Drawing Search is live** for the design and technical teams, out of UAT and on the portal menu, ahead of its date. **Client Briefing is back on the agenda**; Muhammad has resumed it. The shared workstation is still not ordered.


WORKSTREAM	WHAT IT DELIVERS	OWNER	NEXT DATE	STATE
1 · ESTIMATING	SDI Estimating Intelligence Drawings in, costed workbook out	J. Gray	Sep / Oct 26	PARALLEL RUN · 11
2 · TECH DESIGN	SDI Technical Design Intelligence Document Manager tools, then an in-house PDM	Y. Kumar	29 Sep 26 · P2	P2 HARDENING · P3
3 · CREATIVE	SDI Creative Design	M. Yazir	Now	LIVE BACK ON

WORKSTREAM	WHAT IT DELIVERS	OWNER	NEXT DATE	STATE
	Intelligence Drawing search live · client briefing back on			
SHARED	SDI shared workstation Hosts all three · Linux and Windows side by side	J. Gray	Quotes to finalise	NOT ORDERED · WA

01 The programme on one axis

Three workstreams, three owners, one calendar. Re-drawn from the 4 September trackers and the 11 and 16 September updates.

ALL WORKSTREAMS · 1 JUL 2026 → 28 FEB 2027

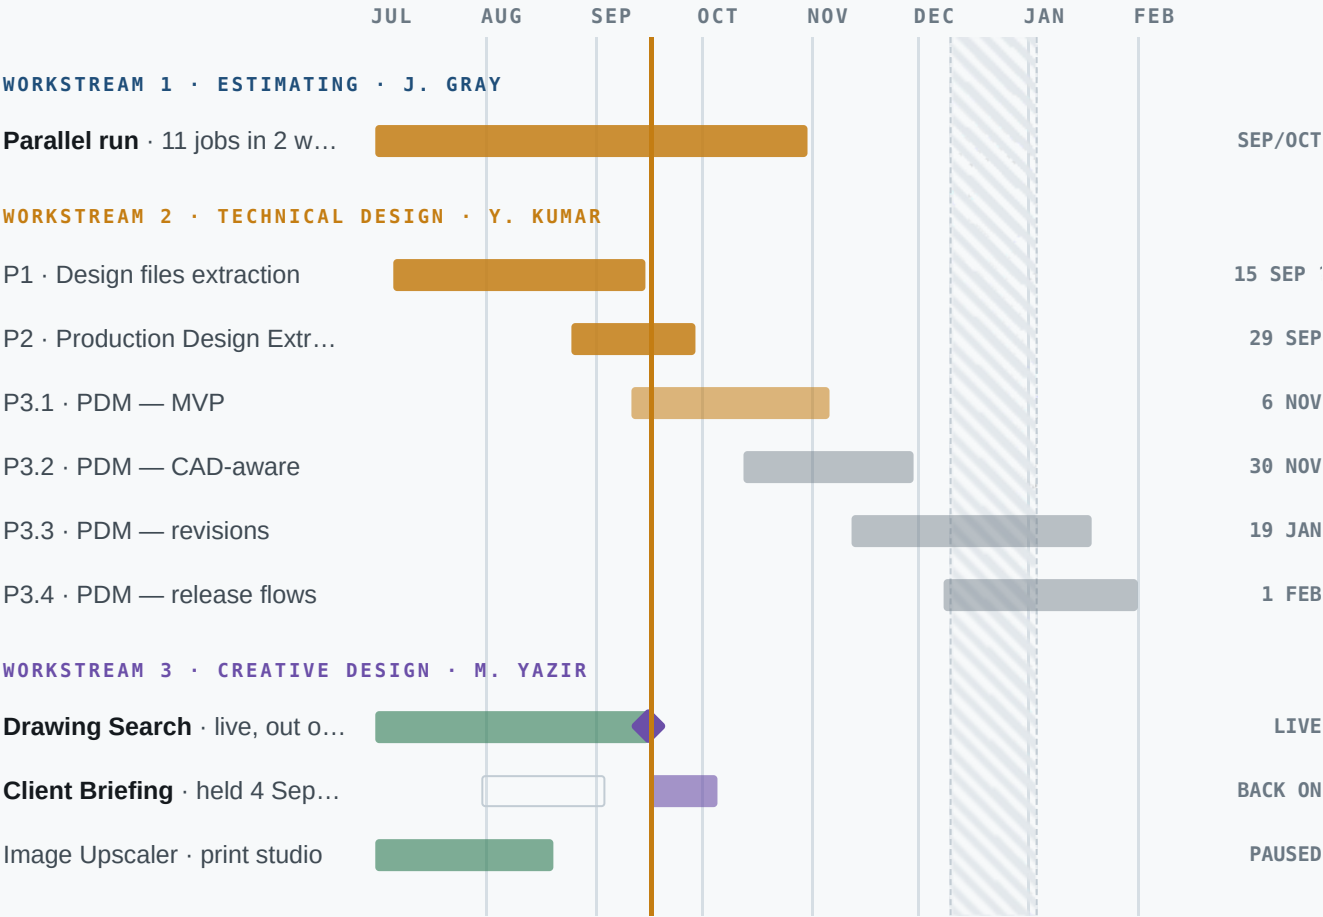

IN PROGRESS DELIVERED IN-HOUSE PDM CREATIVE DESIGN WAS ON HOLD GO LIVE

DEVELOPER LEAVE · 10 DEC — 4 JAN

What moved since 7 September

The estimating loop closed. On 7 September one job of five had come back. Now all three estimators have returned reviews — Howard on the M&S graphic holder and the Harrods stand, Tony on the sunglasses tray, Tim on three jobs — and eleven jobs have run in two weeks. Every finding is in the engine as a rule with the estimator's name on it, and none of it as a figure copied off a sheet. The go-live target is unchanged and the thing that decides it is now moving: reviews returned, at six a week.

The programme's first go-live happened early. Drawing Search was tracking 25 September; it is live for the design and technical teams now, out of UAT, and on the portal menu. The 7 September report's "no buffer on the first go-live" risk is closed.

One line restarted. Client Briefing, on hold from 4 September, is back on the agenda from 16 September with Muhammad working on it, in a smaller and more useful shape than the tracker priced. No date is claimed for it yet.

P2 keeps 29 September and P3.1 has started. Yogesh's week went on hardening Production Design Extraction after its approval, and Ubuntu and Docker are installed for the PDM MVP. P1's 15 September date has passed and the 11 September report does not state it as live; that is asked below rather than assumed.

The workstation slipped. It was needed by 10 September and is not ordered; the server and hardware quotes are still to be finalised. Yogesh's watch-point, and now the programme's.

The KTP presentation is in preparation, Muhammad Yazir with James Gray. It carries the plan for each workstream and live demonstrations of what is already running — the estimating engine on a real drawing pack, the drawing library on 32,422 sheets, the Document Manager tools and the client briefing template. Every item in it is working software rather than a proposal.

02 Workstream 1 — SDI Estimating Intelligence

STATUS	OWNER	WITH	TARGET GO-LIVE
Parallel run	J. Gray	James Ryan · Dave's estimators	SEPTEMBER / OCTOBER 2026
decided on reviews returned, not on what the engine can do			

Deterministic cost-estimating engine — a CAD pack in, a costed workbook on the estimators' own template out, with a covering e-mail, a job report and a customer quote. Every priced line names its source. Since 7 September: about 270 commits, and the

test suite stands at 5,940 passing — and the tests now execute the engine rather than read its source.

Eleven jobs in two weeks, and the feedback is in

The 7 September report's ask was five back for five out. What came back was better than the count: **every estimator has now reviewed the engine's work on their own job**, line by line where it mattered, and replied. Nine of the eleven jobs are named below. Six more run this week, among them **11650-06, the Boots Coffret hospital kit** — asked for by Tim on 16 September at **quantities 2 and 18**, and with the **route and the bill of materials** wanted alongside the cost, which is the first time the route has been asked for as a deliverable in its own right.

THE FORTNIGHT, COUNTED	
11 jobs run in two weeks · against a minimum of five a week	3 of 3 estimators returned a review · six job-reviews between them
~40 points raised · every one now a rule, not a patch	69 numbered decisions · D-016 to D-082, each with its source and proof
5,957 tests passing · across 381 files, executing the engine	272 commits · since the 7 September report
0 of 3 supplier price lists loaded · every unpriced bought line traces here	0 of 11 parity comparisons filed · see below

JOB	WHAT IT IS	WHAT THE REVIEW FOUND, AND WHAT THE ENGINE NOW DOES	ESTIMATOR
0355255 10975-02	Table-top graphic holder (M&S) acrylic and steel, asked	Howard asked for the quantity breaks on one sheet with the formulas showing, the tape priced by the length used rather than as three strips at pack prices, and the right number of holders per sheet. All in: the estimators' own price-break tab is filled, a Quantity Breaks tab recalculates at every quantity, roll goods are priced by the metre cut, and the base sheet is	RETURNE

JOB	WHAT IT IS	WHAT THE REVIEW FOUND, AND WHAT THE ENGINE NOW DOES	ESTIMATOR
	at 10, 50, 250 and 1,000	deliberately run at one unit so each department's set-up is visible. One labour line remains for Howard to rule on.	
7332-01	Signage stand (Harrods) plated welded frame, square-tube leg, acrylic lens	Howard's sheet has five laser rows where ours blended two parts into one rate; each component now has its own row at its own rate, and components the nesting proves share a sheet share one set-up. Production runs 1.0 mm steel where the drawing says 0.9; a mitred tube leg is sawn, not bent; a plated part is packed out and packed back as two operations; brushing before plating is named. Plating and the freight to the plater are shown as awaiting current quotes , not as a figure from a sheet. Second run assessed 16 Sep; a short list is still open (below).	RETURN
11908-21	Sunglasses tray 9 mm laminated MDF · 400 × 390 mm	Tony's finding was that whole joinery operations were missing: edge banding, saw and spindle, bench work, set-up amortised over the quantity. The engine now mints saw and spindle work from the drawing's own words, gives a board assembly its bench-fitting line, holds the edging specification with its rate from the supplier catalogue, and separates each department's set-up from its run time. Five more of Tony's jobs are queued as controlled learning runs.	RETURN
12349-02	Gravity feeder modules (Fanatics) acrylic and MDF fabrication with a steel bracket	Returned line by line on 7 September; the three defects it found were fixed the same day and it has stayed matched to Tim's sheet through everything since — it is one of the replay gates every change must pass.	RETURN
11350-02	Comms bar, 100 mm (Boots) 1 and 2 mm mild steel, ticket strip,	Four questions, all of them about where a figure came from or why one was missing. Two are answered by arithmetic that reproduces the booked row: the pemming time is 15 seconds a pressed fastener, which is his own 12120 sheet read back, and powder is priced by weight and never by RAL. Two were the sheet failing to explain itself — three lines read only "needs a rate" where two of them carried a	RETURN

JOB	WHAT IT IS	WHAT THE REVIEW FOUND, AND WHAT THE ENGINE NOW DOES	ESTIMATOR
	PEM studs · 27 off	code the engine had minted from the description and the third carried a real code that had been asked and found nothing. Both now say which of the two it is , on every job.	
11350-01	Comms bar, the other size (Boots) same construction, different length	Tim's own note: "the same feedback will be the same for 11350-01 as very similar job". Carried with 11350-02 and re-runs beside it.	RETURNED
11762-17	Wire display with perforated-panel clip U-wire, wire stand, bought-in clip	Wire parts costed as wire and formed on the Robomac; the clip with no part code priced from a labelled standard-commodity rate.	AWAITING
11762-02	Steel shelf with vinyl graphic folded 1.5 mm steel, bought-in graphic	The measured bend count from the DXF wins over the model's; packing throughput banded on the shelf, not the graphic.	AWAITING
12552	Infinity drawer 19 SolidWorks parts, 7 assemblies	Fifteen sheet-steel rows reconcile to the workbook; packaging and delivery held at £0 with a named owner.	AWAITING

Eleven jobs, nine named

Tim's three are now attributed: 12349-02, 11350-02 and 11350-01. Two of the eleven are still not named in the sources this report is compiled from, and the estimating page's run ledger is where that is settled. **The count stands; two names are what is outstanding.**

And the ask that goes with the count. Eleven jobs in two weeks is against a minimum of five a week, so the run rate is being met on our side. Several of those eleven are still awaiting a reply. The reviews are what move the go-live date, and they are worth more than another job going out: Tim's fourteen points on 12349-02 became fourteen changes, and his four on 11350-02 became four more.

The rule the reviews were held to

Roughly forty specific findings came back across the six reviews, and the discipline for every one was the same: **the engine learns the method, the route and the evidence; it never copies a figure off an estimator's sheet.** A number from a manual estimate is not a price source, even as a reference, and is retained nowhere — not in the register, the documentation, the reports, the prompts, the tests or the audit record. A price comes from SDI Live, a supplier catalogue or an identified current quote, or the line says plainly that it is awaiting one and who owns it. Written into the change register as its non-negotiable pricing policy, with a test that a new run cannot discover or display a historic manual amount anywhere.

Parity — what we can prove, and what we cannot

Parity is the engine's workbook read against the estimator's own completed sheet, block by block, each side reconciled to its own totals before anything is compared, differences signed both ways, filing a ledger row per job. It runs from the portal against a finished pair, or at run time where the manual sheet is attached up front.

No cell-level comparison is filed for any of the eleven

Because no manual sheet has been attached to a run. The ledger in source control holds one row, from a job in July. **Claiming parity on this fortnight would be the one thing this programme does not do** — the proof is the log, not the theory — so what follows is the estimators' own verdicts rather than a computed variance.

- **Tim on 11350-02:** *"Costs come out really close."* His words, and the closest thing to a parity verdict on a current job.
- **12349-02:** the three defects his first review found were fixed the same day and every line was then reconciled to his sheet. It is held as a replay gate, so no later change can quietly move it.
- **The other nine:** no verdict either way, and that is not a claim of accuracy.

What turns this into a table: one command a job on the laptop against the manual sheet wherever one exists. Each run files a ledger row, and where the engine estimated first, the comparison is added when the manual sheet arrives. **Ask: the manual sheets for the eleven.**

Why no figure off a manual sheet appears in this report. By rule a number from a manual estimate is not retained in the register, the documentation or the reports, so parity is reported as a variance and a direction and never by printing an estimator's own amount.

What landed in the engine

One workbook, every quantity NEW · JAMES

An enquiry asked at 10, 50, 250 and 1,000 now produces **one spreadsheet** rather than one per quantity. The estimators' own Material Price Break tab is filled by the engine and a Quantity Breaks tab recalculates the whole estimate at each quantity, with order-level freight divided by that quantity instead of a pallet landed on every unit. The base sheet is deliberately run at one unit, where each department's set-up is visible rather than hidden inside a volume average.

"Still generating multiple s/sheets" — 15 Sep. The break tab was already doing its job in the first workbook; the old per-quantity mechanism was still filing copies underneath it. The sweep still computes the figures the tab and the report read — it simply stops filing the copies.

Every quantity on one workbook NEW · HOWARD

The estimators' own **Material Price Break** tab is filled by the engine, and a **Quantity Breaks** tab recalculates the same estimate at every quantity the enquiry asks for — 10, 50, 250 and 1,000 on the graphic holder — with the formulas showing, as Howard asked. The base sheet is run at one unit deliberately, so each department's set-up stands visible rather than hidden inside a volume average.

Roll goods are priced by the length used NEW · HOWARD

Tape, edging and anything else sold by the metre is priced by the length cut off the roll, and the roll price is asked of SDI Live on each run. Howard's tape had been three strips at three pack prices. Generic: it fires on every job with a roll-good, not on his.

One laser row per component, one set-up per proven sheet NEW · HOWARD

Each laser-cut component gets its own labour row at its own rate, as the estimators' sheets do. Set-up is shared only where the nesting proves the components sit on one stock sheet — the proof is the engine's own nest arithmetic, and where it fails each component carries its own set-up. On the Harrods stand's second run, the five rows landed; the shared set-up on two of them did not, and is on the open list.

What the shop knows that the drawing does not say NEW · HOWARD

Five production rules, each a confirmed decision with the estimator's name and date on it, each visible on the line it changes and overridable by an estimator: production runs **1.0 mm steel where a drawing calls for 0.9**; a mitred square-tube leg is **sawn, not bent**; welds are **dressed or not by the customer's own standard** (M&S yes, TTI no); a plated part is **packed out and packed back** as two operations; **brushing before plating** is a named operation. A rule of this kind cannot be outvoted by the drawing readers, which is what had kept the 0.9 on one part.

The joinery route exists NEW · TONY

Saw and spindle work minted from the drawing's own words (a rebate gets the spindle); a board assembly gets its bench-fitting line; the **edging specification** is held as a specification with its rate from the supplier catalogue; and every department's set-up is separated from its run time — a convention Tony's sheet and Howard's both confirm, so it is shop-wide. A guard is queued for Tony's next jobs: a purchased, customer-supplied or pre-assembled board parent must not be given bench work merely for having child records.

An unpriced line says whose gap it is NEW · TIM

Three lines on Tim's comms bar read "NOT PRICED — needs a rate", and his reply asked the question that wording had failed to answer: is the spec missing from the drawing, or can the system not find a cost? They were not one case. Two carried a code **the engine had minted** from the description because the pack gives none for a wing nut or a PEM stud — nothing can be looked up against a code we wrote, and the placeholder sits in the code column looking like a part number. The third carried **DBR60, a real code**, which was asked and came back with nothing. Each line now says which, because the answers differ: one is closed by a code on the pack, the other by loading the purchasing catalogue. Fires on the shape of the line, so it reaches every job with a bought item.

Underneath it, the standing item. No supplier price list is loaded into the purchasing catalogue yet, so a bought line with a perfect spec still finds an empty shelf. Elite, Eagle and Thermaset remain the action.

Where a figure came from, in arithmetic that reproduces it NEW · TIM

Tim asked where the pemming rate and the powder cost come from. Both are now answered on the record rather than in an e-mail. **Pemming** is the MANM department rate against 15 seconds a pressed fastener — which is his own 12120 sheet read back, where 4 clinch nuts at 60 units an hour and 2 PEM studs at 120 both come to 240 inserts an hour. **Powder** is priced by weight and the colour never enters the sum: coated area, times a coverage figure, times the per-kilo rate. In both cases the stated constants reproduce the booked row exactly, which is the test a figure has to pass before it is allowed to stand.

Three figures go back to him to rule, because each came off one sheet or is our own derivation: the per-kilo powder rate, the coverage (we hold one figure, the workbook template's own calculator holds another a fifth apart), and the 15 seconds. His proposal to put the powder reference on the drawing is accepted in principle — it prices the line from a real SKU instead of an average and retires two of the three questions.

The change register is the operating contract DONE

Every rule above is a numbered decision, **D-016 to D-082**, recording who ruled it, on which job, whether it is generic or a scoped pilot from one job, where it is implemented and the test that proves it. It is the hand-off document for the estimators: what the engine believes, why, and who said so — so the same question is never asked twice.

Why it matters. Proof is the log, not the theory. A change that only fires on the job it was found on does not ship.

The Harrods stand's second run, assessed 16 September

IN PROGRESS

Landed: five laser rows per component on template rates, weld and dress times as Howard stated them, the pack-to-plater rows, plating and freight carried as awaiting quotes. **Not yet:** the shared laser set-up on two nested parts, the brushing minutes on the frame, the pack minutes on the frame, a tube-bend flag still on the sawn leg, and the plating specification not identified on the run. One of these was diagnosed and fixed from the book alone; the rest need the run's own record from the laptop, which has been asked for.

After the parallel run — unchanged from 7 September

The automated pipeline and on-demand controls stand as described last time: one button imports the full and latest drawing pack, one click generates the estimate with its explains and e-mails it with the quote, parity at the time of the run or added afterwards. In now: amend the estimate and regenerate the quote; print the pack from the portal. No timetable yet for China quotations or multi-PDF packs. Nothing here moved this period; the period went on the reviews.

03 Workstream 2 — SDI
Technical Design Intelligence

STATUS

P2 hardening · P3.1 started

OWNER

Y. Kumar

RESOURCE

Sole developer

NEXT GO-LIVE

29 SEPTEMBER 2026

P2 · Production Design Extraction

Two threads. The **Document Manager tools** read SolidWorks project data without a SolidWorks seat and pull the right drawing pack into the estimating app (P1) and the shop-floor Production folder (P2). Then an **SDI in-house PDM** in four phases. Not an integration with the SOLIDWORKS PDM vault; SDI is building its own, on GitLab and LFS.

The week to 11 September, in Yogesh's report

P2 hardened after its approval IN PROGRESS

- **The two checkouts untangled** — UAT on port 8000, the feature branch on 8001 — so user testing and development stop treading on each other.
- **The licence key and password-less e-mail fixed.**
- **Fifteen missing BOM previews diagnosed:** twelve were library hardware pointing at a folder that did not exist, now repointed and verified; three are sheet-metal parts that must be re-saved in SolidWorks.
- **The project-10975 crash traced** to stale SolidWorks lock files being opened as assemblies.
- **Gained:** extraction history, diagnostics and a metrics endpoint; live mismatch alerts in Step 4 with recorded acknowledgement; richer e-mail notifications. The test count went from about 240 to **363**.

The drawing packs get prepared for manual estimating too SCOPE

The same tool that collects the correct, current drawing pack for a job is to serve **both sets of estimating** — the AI engine and the estimators working by hand. Dave's team stop assembling packs themselves whether or not a job goes through the engine.

Why it is worth naming separately. Every other benefit on this programme is gated on a go-live. This one is not: it lands as soon as the tool does, for people who are not otherwise touched by the engine, and it is the clearest answer to "what does this workstream do for the estimators today".

Six demo videos, for review without meetings DONE

Short recordings with write-ups covering the SolidWorks COM API, the file-extraction endpoint, the Document Manager API proof of concept and P2 itself. Anyone who needs to see what a tool does can, without booking the developer.

The design meeting's action list ACTIONS

From the weekly meeting with Ian B and Ed Cooper: **ISO release traceability** (who released a drawing and when); **overwrite behaviour on re-run**; an **isometric preview image** for the estimating quote page; a **"promote drawing files" button** so estimating reuses the same back end; and **staging for self-service testing**. Each is a requirement on P2 or P3, not a new project.

P3.1 has started: Ubuntu and Docker are installed for the PDM MVP STARTED

The environment for the in-house PDM's first phase is up. The Design Vault proof of concept was to run on the shared workstation from 10 September; the workstation is not ordered, so where this environment sits is a question for section 05.

The plan, as it stands

REF	PHASE	WHAT IT GIVES YOU	DATE	STATUS
P1	Design files extraction Document Manager API	The correct drawing pack for a job straight into the estimating app. Serving it since 24 August; James was the user tester to 10 September.	15 Sep 26	NOT CONFIRMED LIVE
P2	Production Design Extraction Document Manager API	Collects the shop-floor drawing pack on its own, with a why-not-copied report. Feature branch merges to main w/c 21 Sep.	29 Sep 26	HARDENING
P3.1	PDM — trustworthy files In-house, phase 1	Check-in and check-out, versioning, locking and history.	6 Nov 26	STARTED
P3.2	PDM — CAD-aware In-house, phase 2	Where-used, missing references, version consistency, released-reference checks.	30 Nov 26	NOT STARTED
P3.3	PDM — engineering revisions In-house, phase 3	Approval workflow: WIP → pending approval → released, not approved, obsolete.	19 Jan 27	NOT STARTED

REF	PHASE	WHAT IT GIVES YOU	DATE	STATUS
P3.4	PDM — release workflows In-house, phase 4	Separate release routes for WIP, prototype and production components.	1 Feb 27	NOT STARTED

Watch-points, in Yogesh's words

- **One to two days absorbed** by demo preparation and the design team's new e-mail and history requirements. P2 keeps 29 September; the days come out of the next build, as the 4 September re-plan allows for.
- **The server and hardware quotes are still to be finalised** before designers and estimators get test access. This is the shared workstation of section 05, and it is now the item on this workstream's critical path that is not in its owner's hands.

The lever is still a second pair of hands. Every date from P3.1 onwards depends on one person being available, and leave from 10 December to 4 January sits inside them.

04

Workstream 3 — SDI Creative Design Intelligence

STATUS	OWNER	PROJECTS
Drawing Search live	M. Yazir	1 live · 1 back on · 1 paused
FIRST GO-LIVE DELIVERED · SEPTEMBER 2026 ahead of the ~25 Sep tracker date		

SERVICE NAME	TRACKER NAME	FOR	POSITION	LIVE
SDI Drawing Search Intelligence	Fixture Library	Design and technical teams	LIVE · OUT OF UAT	Sep 20
SDI Client Briefing Intelligence	Client Briefing	Jonathan · the four teams	BACK ON · 16 SEP	not c

SERVICE NAME	TRACKER NAME	FOR	POSITION	LIVE
Image Upscaler	Image Upscaler	Sarah, Dean	PAUSED AUG 26	—

Drawing Search is live, out of UAT, and on the portal LIVE

Live for the design and technical teams. It searches **32,422 drawings** by what is actually printed on the sheet — the client, the material, the finish, the RAL, the job number, a line from a note — and from the same screen a designer opens the SolidWorks or 3ds Max file straight into the software rather than hunting through folders. **Ian tested it and liked it, which is why it went in.** Muhammad's fixes this week all came from watching real use: opening the right drawing, and not hiding drawings filed in unusual places — this year's Boots Dynamix drawings were not showing at all and now are.

It has been added to the SDI Intelligence portal as **SDI Drawing Search Intelligence**, directly below its user guide, on the laptop and on the server. The IIS/nginx production home with AD sign-in and the index on the K: drive remains the plan; the address on the menu is the one to use until then.

Next. More designers on it on real jobs. The index grows as drawings are filed, and a drawing filed in an unusual place is a bug to fix, not a limitation to accept. The 7 September "no buffer on go-live" risk is closed by the go-live.

It is not yet integrated with SDI Intelligence NEXT

The search runs as its own web application. The portal **links** to it rather than containing it, and the two systems do not yet share anything but a menu entry. Joining them is what turns a drawing found in the library into a part code the price chain already understands — the point at which finding the fixture and costing it become one action rather than two.

Stated as a gap rather than left implied, because the menu entry makes it look joined up already.

Client Briefing is back on the agenda

RESUMED · 16 SEP

The 7 September report had it on hold from 4 September, to be re-planned as agents by James Gray and Yogesh Kumar. **Muhammad has resumed it**, in a smaller shape than the tracker priced: it takes a brief however it arrives — e-mail, a recorded call, a WhatsApp voice note — and turns it into one consistent brief: which of the four teams it belongs to, what can be filled in from what SDI already knows about the account, and what is still missing, separating what blocks work from what can follow. **It never books anything itself; every brief goes to Jonathan to approve.**

Honestly early: two briefs through it, both Muhammad's own, none yet on live work. What it needs is time with Jonathan and real briefs. The tracker's dates — sign-off 21 Sep, build to 15 Oct, release ~Nov — are kept for the record and not re-claimed.

More exists than the status implied. It is not restarting from a blank page:

- **A web template, already developed** — being enhanced now rather than designed.
- **An e-mail AI agent analysing client communications**, which is what lets a brief arrive as an e-mail, a recorded call or a voice note and still come back structured.
- **Design and account manager details collated** against the brief, so the right people and the account's own history travel with it.
- **The purpose, stated plainly:** to promote communication and collaboration across the four teams — one consistent brief, the gaps named, and nothing booked without Jonathan's approval.

The manufacturing business analysis continues alongside

CARRIED

Muhammad's business analysis for the Manufacturing / CNC SDI Intelligence automations — the live production spreadsheet for BOMs and routes on its way into Sage X3, the design DXF process onto CNC machining, as a BRD and user stories with James Gray — carries on beside the two projects above. No dates are claimed for it until that record exists. Nothing on it is reported this period.

SDI Drawing Search Intelligence · phase detail

#	PHASE	START	END	DURATION	STATUS	NOTES
01	Proof of concept	1 Jul 26	1 Jul 26	1 day	DONE	Prototype demoed to & Stuart.

#	PHASE	START	END	DURATION	STATUS	NOTES
	Stakeholder validation					Green light received.
02	Development — round 1 Full build	2 Jul 26	31 Jul 26	4 weeks	DONE	Search, PD indexing, GPU support, Flask UI, scan cache
03	Unit testing Internal — developer	1 Aug 26	2 Aug 26	2 days	DONE	Search accuracy, edge cases, GPU fallback, network safety.
04	Integration testing — round 1 Live data test	3 Aug 26	7 Aug 26	5 days	DONE	Finding: Renders folders not indexed. Set back to dev
05	Development — round 2 Fixes & hardening	1 Sep 26	15 Sep 26	2 weeks	DONE	Delivered in UAT; this week's fixes came from live use.
06	Integration testing — round 2 Re-test after fixes	15 Sep 26	20 Sep 26	5 days	ON LIVE USE	Overtaken by the go-live; what it was to verify is now verified by designers on real jobs.
07	UAT User acceptance testing	7 Sep 26	25 Sep 26	3 weeks	DONE	Studio designers tested on real projects; later tested it and

#	PHASE	START	END	DURATION	STATUS	NOTES
						went in. Out of UAT ahead of the end date.
08	Go live Studio-wide rollout	Sep 26	—	—	LIVE	On the port menu. IIS/nginx deploy with AD authentication and the K: drive index remains the production home.

Image Upscaler PAUSED AUG 26 · 56%

Unchanged. Paused on studio priorities, not on any failure; the CMYK conversion it produced remains in daily use. Restartable when capacity allows.

05 The shared workstation

One machine, three workloads, two operating systems. Specified from measurement on 3 September; needed by 10 September; **not ordered**.

REQUEST	BUDGET	SUPPLIER	
1 × workstation	£4,800–5,050 ex-VAT	Scan 3XS	
			WAS NEEDED BY 10 SEPTEMBER 2026 quotes still to be finalised

Where it stands

The 7 September report said "order this week" with two decisions in front of it: whether it can sit on the same LAN as sdi-dc01, and whether AD integration for Drawing Search is firm. Neither decision is recorded as taken, the server and hardware quotes are still to be finalised, and the date it was needed by has passed. Yogesh's watch-point puts it plainly: designers and estimators do not get test access to the Technical Design tools until it exists.

What changed underneath it. Drawing Search went live without it, on its current host; and P3.1's Ubuntu and Docker environment is installed, on a machine this report cannot name. The three workloads it was sized for are all running somewhere; the always-on, same-LAN home they need is what is missing.

Estimating engine · J. Gray

Running on a laptop. Needs 38 GB and the fastest single core available: SolidWorks and Excel are single-threaded, and it drives both through an interactive Windows desktop.

Drawing Search · M. Yazir

Live now, on its current host. Must become always-on and sit beside the file server for the production home; a 16 GB SolidWorks-certified GPU is the one line this turns on.

Design Vault / PDM · Y. Kumar

Two Ubuntu guests for GitLab and PostgreSQL under Hyper-V, with a Windows Server guest later. P3.1's environment is installed; where it lives permanently is this machine.

The shape, unchanged

- **CPU** — AMD Ryzen 9 9950X: the fastest single core, not the most cores.
- **Memory** — 128 GB as 2 × 64 GB ECC, two slots free to reach 256 GB.
- **GPU** — 16 GB SolidWorks-certified card.
- **Always-on** — mirrored NVMe system disks, a 4 TB data disk for the Git LFS volume, and a UPS.
- **Windows 11 Pro on the metal**, Ubuntu as Hyper-V guests. Not Windows Server, because SolidWorks is unsupported on it.

06 Sage X3 data migration

STATUS	OWNER	WITH
Plan, gated	J. Gray	Acuity · the data owners

ALL DATA IN X3
FRIDAY 30 OCTOBER 2026
the ERP itself goes live 4 Jan 27

The Access database behind SDI Live moves to **Sage X3**. Eleven X3 templates are covered by built extract views drawing on eighteen core source tables; everything else in the roughly three hundred tables — and the Crystal Reports layer sitting on top of them — needs a stated disposition even where that disposition is “not migrated”, because a table with no decision against it is how one survives a migration by accident. This section is the consolidated view.

Two dates, and they do not conflict

All data in X3 by Friday 30 October 2026. The ERP itself goes live **4 January 2027**, which is the date on the programme timeline in section 01 and is not SDI Intelligence's to move. The migration finishes first on purpose, so the business loads a system it has already proved rather than proving one during cutover.

Where these figures come from. The row counts and dispositions are the SDI Live extract and the analysis run against it. Where a number is derived or approximate the table says so, and the three things not yet known are listed at the end rather than filled in with a guess.

Mapped to Sage X3 — eleven templates, eighteen source tables

Built extract views, proven against the source, grouped by the category an owner would recognise rather than by template code.

SAGE TEMPLATE	WHAT IT CARRIES	SOURCE TABLE(S)	ROWS
PRODUCTS / ITEMS			
ITM	Products	STK_STOCK + ASC_PMA_TBL	41,330
ITF	Product sites	STK_STOCK + ASC_PMA_TBL	41,330
BILLS OF MATERIAL			
BOMP	Bills of material	ASC_BOM_TBL	61,648 lines 14,581 parents
CUSTOMERS / SALES			
BPC	Customers	SL_ACCOUNTS + ASC_SL_ADDRESSES + SL_TERMS	500
SOH	Open sales orders	ASC_COR_TBL	1,159 £13,535,254
SUPPLIERS / PURCHASING			
BPS	Suppliers	PL_ACCOUNTS + PL_ADDRESSES	1,218
POH	Open purchase orders	ASC_POR_TBL	1,166 £5,675,222
FINANCE • LEDGERS			
BICX	Open accounts receivable	SL_TRANSACTIONS	843 ~£6.68M net
BISX	Open accounts payable	PL_TRANSACTIONS	2,151 £5,125,595
GAS	General ledger trial balance	SL_PL_NL_DETAIL	derived nets to ~0

SAGE TEMPLATE	WHAT IT CARRIES	SOURCE TABLE(S)	ROWS
---------------	-----------------	-----------------	------

STOCK

SMR	Stock opening balances	STK_STOCK + ASC_LOT_TBL	~40,000
-----	------------------------	-------------------------	---------

Routings are not in the eleven

Works-order routings were parked earlier in the programme. **If they are now in scope for the October go-live that is a scope addition**, and it changes both the disposition table below and the load waves in week three. This needs an answer before the plan is final.

Every other table, and what happens to it

Roughly three hundred source tables were analysed. Nothing is left without a disposition.

GROUP	WHAT IS IN IT	VOLUME	DISPOSITION
Core mapped	The eighteen source tables behind the eleven templates above	18 tables	MIGRATE — built and proven
UDEF family	SDI's own additions to the Access schema. Populated: UDEF_WO_SHORTAGE_FROM_ORC (13,453), UDEF_COR_DATE_HIS_TBL (9,790), UDEF_ASC_ORC_ITEMS_T (4,810), UDEF_div_PL (490), UDEF_ASC_SOR_TBL_SC (449), UDEF_ASCSORTBL_68530446 (324), UDEF_TEMP_SL_COUNTRY (230), plus dated UDEF_ASC_DVY_TBL_* and UDEF_ASC_POR_TBL_* variants and UDEF_tab_Generic* config (0–4 rows)	~30k rows	REVIEW — some are custom fields on live records and belong in X3 user fields, others are staging or temp and drop. Not yet analysed ; week-one task
Other ASC operational	Works orders ASC_WOR_TBL (53k), ASC_WKK_TBL (231k), job costing ASC_JBC_TBL (233k), kitting ASC_KIT_TBL (270k), deliveries	~1.9M rows	DISPOSITION NEEDED — each is migrate, rebuild natively in X3, archive or

GROUP	WHAT IS IN IT	VOLUME	DISPOSITION
	ASC_DVY_TBL (144k), invoice detail ASC_INV_TBL (82k), planning ASC_PLN_TBL / ASC_MRP_*, capacity ASC_CAP_TBL (71k), labour ASC_LTU_TBL (814k) and ASC_TBI_TBL (64k)		drop. Tied to the routings question above
Finance detail and history	SL_PL_NL_DETAIL (1.2M), NL_TRANSACTIONS (244k), sales and purchase transaction and allocation history	~1.5M rows	ARCHIVE — the openings cross as GAS; the history does not follow
Audit and quote history	ASC_HIS_TBL (1.6M) and the quote- history family	~1.6M rows	ARCHIVE — cold storage, and available to the estimating engine as comparables rather than to X3
Duplicates	_2 / _3 / _4 variants and dated backups of live tables	29 tables ~3.5M rows	DROPPED — confirmed, already out of scope
System, config and reference	SYS_*, MetaData.*, Diagnostics.*, language labels, error logs, Workspace.*, UITest.*, sfdc.*, AIEstimating.*	~40+ tables	DO NOT MIGRATE — rebuilt natively or irrelevant. Reference data (currencies, countries, units of measure, VAT) is confirmed or rebuilt, not copied
Crystal Reports	The reporting layer sitting on the Access database. These are .rpt files , not tables , so they were never in the table dump	inventory not captured	REBUILD OR RETIRE — nothing migrates; each report is identified, its source tables traced, then rebuilt in X3 reporting or retired with an owner. Register is a placeholder until the inventory exists. Due by end of October


Data quality, by number

HEADING	NUMBER	WHAT IT MEANS
Good data — in scope and mapped	18 tables → 11 templates	Extract views built and proven against the source
Duplicates — dropped	29 tables ~3.5M rows	Dated backups and _2/_3/_4 variants; removed from scope, not cleansed
Do not migrate	~40+ tables	System, log, audit, API staging and transient MRP
Archive — not to X3	~3.1M rows	Audit and quote history, and the ledger detail behind the openings

And the record-level issues, which are the ones that take people's time. These are not sign-offs.

RECORD-LEVEL ISSUE	COUNT	OWNER AND ACTION
Items with a blank description — half the catalogue	20,724	Biggest open issue. Products / stock. Real record-level work
Items with a zero base price	36,650	Expected for raw and sub-assembly lines; the finished goods among them are what need checking
Sales-order lines with a blank COR_ORDER_STATUS	23,082	Sales order manager — one decision, then it applies to all of them
Duplicate part-master records	66	Products / stock
Customer category or tax mismatches	40	Credit control
Supplier category or tax mismatches	34	Accounts payable / procurement
Customers with a blank postcode	74	Credit control
BOM orphans	51	Engineering — non-blocking, but confirm the active set

The plan — three weeks to all data in X3

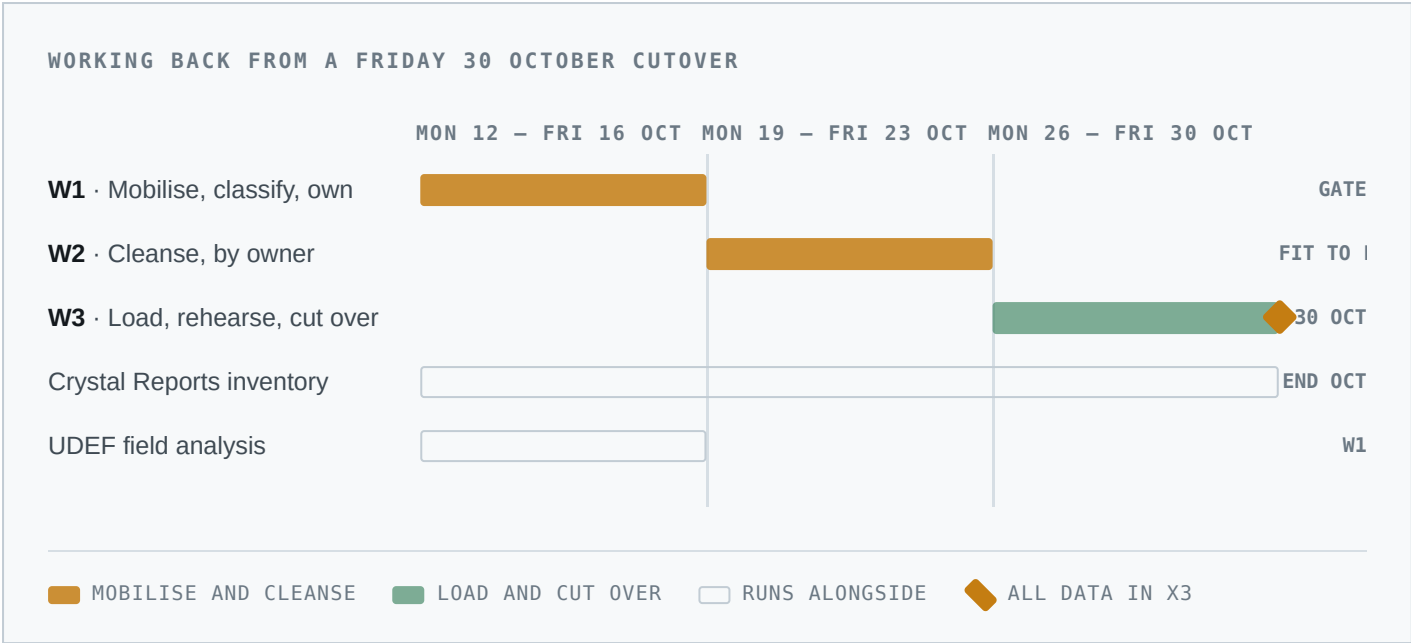

WEEK 1 · MON 12 – FRI 16 OCT	OWNER
Confirm and assign a business owner for every data area	James Gray
Lock the classification per table — good, duplicate, bad, do not migrate	James Gray + owners
Clear the three outstanding third-party items — the sign convention (which blocks the final BICX and BISX extracts), non-production environment access, and the product-category confirmation, plus multi-site	Acuity
UDEf analysis — run the column-definition query across the populated UDEf family, then decide field by field: a custom field on a live record (map into an X3 user field) or staging and temp (drop)	James Gray
Open the Crystal Reports inventory — capture the .rpt filenames, the reports-menu export or the folder listing, and start the register	James Gray + report owners
Run parity and QA over the eleven built views; apply any fixes	James Gray
Chart of accounts confirmed pre-loaded, or imported	Acuity / Finance

WEEK 2 · MON 19 – FRI 23 OCT · CLEANSING, IN PARALLEL		OWNER	THE ACTUAL
Finance — general ledger, AR, AP		Charlotte (FD)	Tax codes (0), the ID a lists, AR an reconciled t reports
Products and items		David / stock manager	20,724 blar descriptions: prices, 66 c records, ca sanity-chec
Bills of material		Engineering	51 orphans confirm the
Customers		Credit control	74 blank pc mismatches
Suppliers		AP / procurement	34 mismatc EMP list, ac
Open sales orders		Sales order manager	The blank COR_ORD decision — ride on it
Open purchase orders		Procurement	Confirm the
Stock		Stock controller	Snapshot a lot level
Crystal Reports		Report owners	Catalogue e source tabl fields, rebui named own
WEEK 3 · MON 26 – FRI 30 OCT		WHAT HAPPENS	
Mon 26		Trial load master data — BPC, BPS, ITM, ITF, BOMP — into non-production; reconcile counts	

Tue 27	Fix rejections; trial load the transactions — SMR, GAS, BICX, BISX, POH, SOH
Wed 28	Dress rehearsal: a full timed run against a frozen snapshot, with owner spot-checks
Thu 29, evening	Access goes read-only; cutover snapshot taken; all waves loaded
Fri 30, morning	Go / no-go. The FD signs the trial balance, the stock value, AR and AP, and the sales and purchase order totals — then live

A note on the calendar. The plan as first drafted ran “13–17, 20–24, 27–31 October” with a Friday 30 October cutover and a go / no-go on Friday the 31st. 13 October 2026 is a Tuesday and 31 October is a Saturday, so those could not all be true. The three working weeks that end on a Friday 30 October cutover are the ones above.

End of October is a target with a gate, not a commitment

Three things have to hold and two of them do not hold today.

- **The third-party items must clear in week one.** The sign convention blocks the final AR and AP extracts, and without non-production access and the product-category confirmation the trial load cannot run in week three.
- **Cleansing is real work, not sign-off.** 20,724 blank descriptions and the blank sales-order-status decision are record-level effort for the business owners. Three weeks is tight at that volume.
- **Only one trial-load cycle fits.** The original plan had two trial loads plus a dress rehearsal; compressing to a single load, fix and rehearse pass removes the safety net, so any structural surprise moves the date.

The recommendation is an explicit decision point at the end of week one: if those three are not confirmed by **Friday 16 October**, the date rebaselines to mid-November. That is cheaper than defending a date into a failed cutover, by a distance.

Three things genuinely not known

- **The Crystal Reports inventory does not exist.** They are .rpt files rather than tables, so nothing about them is in the table dump. Nothing migrates — each report is rebuilt in X3 reporting or retired — but each needs identifying, its source tables tracing and an owner. Opened in week one, **due by end of October**.
- **The UDEF family has not been analysed.** Some of those tables are custom fields on live records and belong in X3 user fields; others are staging and drop. The column-definition query is a week-one task and the decision is field by field, because deciding without it would be guessing.
- **Routings and works orders: in scope, or still parked?** They are not among the eleven. If they are now wanted for October that is a scope addition and it changes both the disposition table and the load waves. **This needs an answer before the plan is final.**

07 Open across the programme

Ordered by what it costs to leave alone. Items carried from 7 September keep their wording where nothing has changed; items closed since are listed last, so a reader can see the list shrink as well as grow.

Reviews back at the run rate ACT

Eleven jobs went out in the past two weeks against a minimum of five a week, and six more go out this week. Several of the eleven are still awaiting a reply. The go-live target is decided on what comes back, and the first full round has just shown what a returned review is worth: about forty findings across six job-reviews from all three estimators, every one now a rule.

Workstream 1. Ask of Dave's team: six back for six out, and a reply on the ones still open.

The workstation: quotes finalised, decisions taken, order placed ACT

Needed by 10 September and not ordered. Same-LAN placement beside sdi-dc01 (IT) and whether AD integration is firm (Muhammad) are the two decisions; the server and hardware quotes are what Yogesh names as outstanding. Until it exists, designers and estimators do not get test access to the Technical Design tools.

All three workstreams. The one item on every critical path.

Sage X3: three third-party items, by Friday 16 October

GATE

The sign convention, non-production environment access and the product-category confirmation. They gate the whole October data migration: without them the trial load cannot run in the final week, and the date rebaselines to mid-November. Also needed before the plan is final: **the answer on whether routings and works orders are in scope.**

Sage X3. Owner: Acuity, chased by James Gray. Section 06.

P1 was due 15 September — is it live?

ASK

Yogesh's 11 September report carries P2's date and P3.1's start but does not state P1 as live, and its date has passed. This report does not assume it. One line from Yogesh settles it.

Workstream 2.

Jonathan's time on real briefs

ASK

Client Briefing is back on and gated on one thing: a few real briefs run through it with Jonathan, who approves every brief it produces. Two briefs so far, both Muhammad's own.

Workstream 3. No date is claimed until this has happened.

Plating and plater freight on the Harrods stand are awaiting current quotes

OPEN

Both lines are on the sheet, unpriced, each naming who is asked: the plater for the plating specification and price, the SDI transport department for the haulage. Neither carries a figure from anyone's sheet, by rule. Replaces the 7 September item on three indicative rates.

Workstream 1. A labelled hold, never a silent zero.

Three configured rates have no live source

RULING

The board sheet price, the zinc plating rate per kilogram and the section-stock rate per kilogram are held in configuration with no SDI Live, catalogue or quote behind them. Under the pricing policy they should be either sourced or turned into awaiting-price lines with an owner. Recorded against D-078; a ruling is needed.

Workstream 1. James Gray to rule, with estimating.

Packaging and delivery are held at £0 [OPEN](#)

By decision. The lines stay on every sheet at zero with a named owner until the estimators provide their own calculation; the engine then carries it as a house rate.

Workstream 1. Carried from 27 August. Needs a figure from estimating, not from engineering.

Supplier price lists are still not loaded [OPEN](#)

The ingester is built and tested. It needs the actual files: Elite, Eagle and Thermaset. Every catalogue loaded removes estimator inputs permanently and replaces held lines with reproducible prices.

Workstream 1. Carried from 27 August, unchanged.

Drawing Search: adoption is the measure now [OPEN](#)

Live, and the fixes come from watching real use. The value is decided by designers using it on real jobs, and the production home (IIS/nginx, AD, K: drive index) waits on the workstation.

Workstream 3. Replaces "go-live has no buffer".

The W: drive stops being the single source of truth when the Vault goes live [OPEN](#)

Raised at the 3 September meeting; proposed: sync W: on released status. A design decision for P3.1, which has now started.

Workstream 2. Carried.

Workstream 2 has one developer and no cover [OPEN](#)

Unchanged. Every date from P3.1 onwards depends on one person, the demo and requirement days this fortnight came out of the next build, and leave from 10 December to 4 January sits inside the plan.

Workstream 2. Cannot be recovered by re-planning.

Carried, with no change reported

CARRIED

- **The BrightHR client secret has never been rotated.**
- **SDI-APP01** still needs the rotated database password and the configuration script that tells the health check which build it is running.
- **Two price sources wired to empty tables** — rung 3 of the price chain reads a migrated catalogue whose rows were left inactive.
- **Size is not weighted in description matching** — a deliberately failing test.
- **The PDM requirement register is still open** at around 50 items.
- **Which machines get a SolidWorks seat** beyond the estimating laptop.
- **The manufacturing workstream's first written record** — the BRD and user stories; undated until it exists.

Workstreams 1, 2 and 4. Listed so they are not rediscovered; none moved this period.

Closed since 7 September

CLOSED

- **Four estimates awaiting review** — superseded: reviews are back from all three estimators and the ask is now a run rate, not a backlog.
- **Drawing Search go-live has no buffer** — closed by the go-live, ahead of the date.
- **Client Briefing needs its new plan** — superseded: Muhammad has resumed it as brief intake; what it needs now is Jonathan's time, not a plan document.
- **Three rates on 7332-01 labelled indicative** — superseded by the pricing policy: plating and freight are awaiting current quotes with named owners, and no indicative figure from a sheet is carried anywhere.
- **The engine's tests read its source** — the bench and shop-rule tests now execute the engine on a part and check what it books.

SDI INTELLIGENCE PROGRAMME STATUS · COMBINED REPORT · ISSUE 3 · ISSUED 16 SEPTEMBER 2026 · SUPERSEDES 7 SEPTEMBER 2026

SOURCES · SDI INTELLIGENCE COMMIT HISTORY 7 – 16 SEP AND CHANGE REGISTER D-016 TO D-078 · ESTIMATOR REVIEWS FROM HOWARD THURLEY (10 AND 15 SEP), TONY FORD (8 SEP) AND TIM WILKES (4 AND 9 SEP) · YOGESH KUMAR STATUS 11 SEP · MUHAMMAD YAZIR WEEKLY UPDATE · SHARED WORKSTATION CAPITAL REQUEST 3 SEP · SDI LIVE TABLE EXTRACT AND MIGRATION ANALYSIS

ESTIMATING GO-LIVE TARGET · SEPTEMBER / OCTOBER 2026 – DECIDED ON REVIEWS RETURNED FROM THE PARALLEL

RUN

SDI DISPLAYS · LOUGHBOROUGH · WE.ARE.SDI
