

SDI Programme Status

Three workstreams · one
calendar · one machine

ISSUED 7 SEP 2026
SUPERSEDES 27 AUG 2026
OWNERS J. GRAY · Y. KUMAR · M. YAZIR
COMPILED BY J. GRAY

Status across **SDI Estimating Intelligence**, **SDI Technical Design Intelligence** and **SDI Creative Design Intelligence**, eleven days on from the first combined report. Four things moved. The estimating engine went from producing workbooks to a **five-jobs-a-week parallel run** with the estimators, and one job has come back; over the weekend of 5–6 September its four documents were made to read one costed record, and the job report now opens with the decisions still open. Technical Design's second tool was **demoed and approved**, and the PDM phases were re-planned against real deployment days. Drawing Search goes into **UAT on 7 September**, while Client Briefing is **on hold** and its owner moves to the manufacturing workstream. And all three now have a home: **one shared workstation**, to be ordered this week.


WORKSTREAM	WHAT IT DELIVERS	OWNER	NEXT DATE	STATE
1 · ESTIMATING	SDI Estimating Intelligence Drawings in, costed workbook out	J. Gray	Sep / Oct 26	PARALLEL RUN · 5 JOBS
2 · TECH DESIGN	SDI Technical Design Intelligence Document Manager tools, then an in-house PDM	Y. Kumar	15 Sep 26	P1 · 60% P2 · 90%
3 · CREATIVE	SDI Creative Design Intelligence	M. Yazir	7 Sep 26 · UAT	50% · ON HOLD

WORKSTREAM	WHAT IT DELIVERS	OWNER	NEXT DATE	STATE
	Drawing search live in UAT · client briefing on hold			
SHARED	SDI shared workstation Hosts all three · Linux and Windows side by side	J. Gray	Order this week	£4.8–5.05K EX-VAT

01 The programme on one axis

Three workstreams, three owners, one calendar. Re-drawn from the 4 September trackers.

ALL WORKSTREAMS · 1 JUL 2026 → 28 FEB 2027

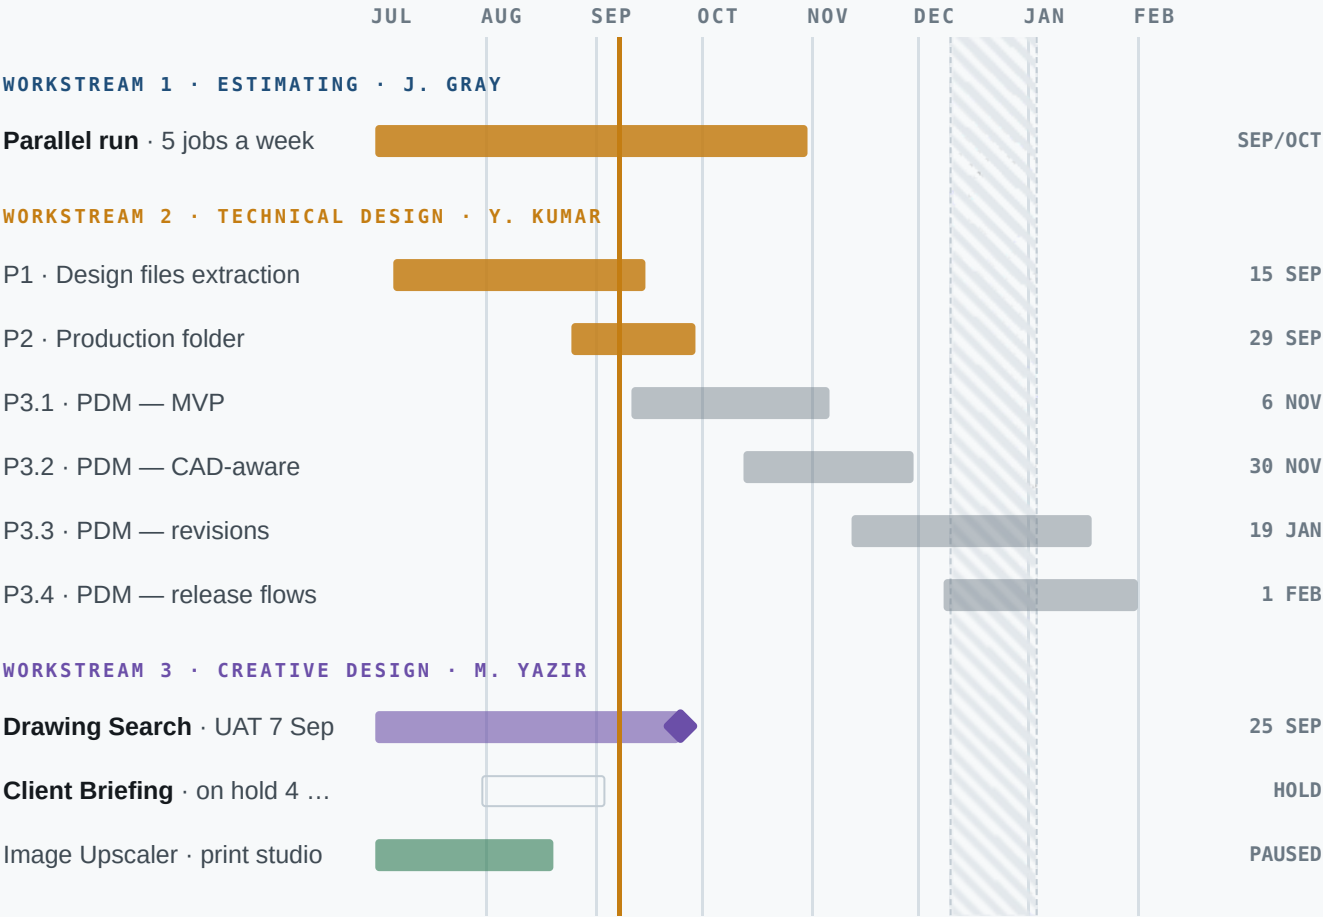

IN PROGRESS DELIVERED IN-HOUSE PDM CREATIVE DESIGN ON HOLD GO LIVE

DEVELOPER LEAVE · 10 DEC — 4 JAN

What moved since 27 August

The PDM dates moved right, and it is not a slip. Yogesh's tracker now interleaves each tool's deployment days inside the next tool's build, so no build occupies a day that is booked for a go-live. P2 goes from 24 to **29 Sep**; the four PDM phases move by one to three weeks and the last lands on **1 Feb 2027**, which is why the axis above now runs to February. P1 on 15 Sep is unchanged.

Three go-lives inside a fortnight, not four inside five weeks. P1 on 15 Sep, Drawing Search on 25 Sep, P2 on 29 Sep. The estimating engine keeps its September / October target, and the thing that decides it is now visible: reviews returned, at five jobs a week.

One line stopped. Client Briefing is on hold from 4 September; its bar ends there. Nothing else depends on it, and it is not deleted — see Workstream 3 for who picks it up and in what form.

The engine's documents agree with each other, and the next phase has a shape. Over the weekend of 5–6 September the workbook, the e-mail, the job report and the quote were made to read one costed record, and the workbook went from nine tabs to five. After the parallel run comes the automated pipeline — one button to import the latest pack, one click to estimate, explain, e-mail and quote — with no date claimed for it until the reviews decide the go-live. Workstream 1 has the detail and a sample page.

The manufacturing workstream has its first job. Muhammad Yazir, with James Gray, maps the live production spreadsheet for BOMs and routes on its way into Sage X3 and the design DXF process onto CNC machining, written up as a BRD and user stories. It stays undated until that record exists.

02 Workstream 1 — SDI Estimating Intelligence

STATUS

Parallel run

OWNER

J. Gray

WITH

James Ryan · Dave's estimators

TARGET GO-LIVE

SEPTEMBER / OCTOBER 2026

decided on reviews returned, not on what the engine can do

Deterministic cost-estimating engine — a CAD pack in, a costed workbook on the estimators' own template out, with a covering e-mail, a job report and a customer quote. Every priced line names its source. Since 27 August: 165 commits, and the test suite stands at 4,274 passing.

Five jobs a week, and the loop that was missing

The 19 August report's problem was that runs went out and nothing came back. The parallel run now has a cadence — **five jobs ran last week, five more are queued for this week** — and the run itself closes the loop: the engine e-mails the finished estimate to the people who asked for it, with the explanation attached, the moment it completes.

JOB	WHAT IT IS	WHAT THE PARALLEL RUN FOUND AND FIXED	ESTIMATOR POSITION
12349-02	Gravity feeder modules (Fanatics) acrylic and MDF fabrication with a steel bracket, 7 off	Engine costed three modules where the enquiry was for one — the GA hangs three on a wall — so £220.91 against Tim's £158.46 was never the same article. A bonded acrylic box came through as one flat where the pack holds seven. Powder priced at £2.14 against Tim's £0.72. All three fixed; every line now matches Tim's sheet.	RETURNED · TIM
11762-17	Wire display with perforated-panel clip U-wire, wire stand, bought-in clip · unit £21.01	Two wire parts were costed as 8 mm <i>sheet</i> because the diameter read as a gauge, and given a laser row nobody would run. Now recognised as wire, costed in the Wire block and formed on the Robomac. The clip, which has no SDI part code, priced from a labelled standard-commodity rate instead of £0.	AWAITING REVIEW
11762-02	Steel shelf with vinyl graphic folded 1.5 mm steel, bought-in graphic	The fold count came from the SolidWorks read (4) where the DXF bend-lines layer measured 5 — the measured count now wins. Packing throughput banded on the vinyl graphic rather than the steel shelf, so pack was 50% too fast. Both fixed.	AWAITING REVIEW

JOB	WHAT IT IS	WHAT THE PARALLEL RUN FOUND AND FIXED	ESTIMATOR POSITION
11908-21	Sunglasses tray (9 mm laminated MDF) 400 × 390 mm · asked at 1, 50, 100, 250 and 500	A parcel-sized tray came back with £95 packaging and £65 delivery because the freight lookup always asked for a pallet. It now asks for what the order is. The assembly line read "Acrylic" on an MDF part; it now books to joinery. Priced at all five quantities from one run.	AWAITING REVIEW
12552	Infinity drawer 19 SolidWorks parts, 7 assemblies · sheet steel, bearings, concrete slab	Fifteen sheet-steel rows now reconcile to the workbook to the penny; the engine's own tab had disagreed with the sheet it wrote. Scrap was being charged on freight. Packaging and delivery came from an AI indication at £85 each — 18% of a £930 unit — and are now held at £0 with a named owner until the estimators supply the figure.	AWAITING REVIEW

One of five returned

Tim's review of 12349-02 is the most useful single piece of feedback the programme has had: it was line by line, and it turned three engine defects into three fixes in a day. **The other four are with Dave's team.** The go-live target is decided on this number, so the ask of estimating this week is the same as the run rate: five out, five back.

What landed in the engine

The finished estimate is e-mailed, automatically

NEW

The estimating page carries a recipients box pre-filled from a saved list. When a run completes, the workbook, report and covering note go to those people with no developer in the loop. The customer quote is **withheld while an estimate is provisional** — it is the one document written to be read by a customer, and it must not leave with a figure nobody has stood behind.

Every pound explained, against the sheet's own totals

NEW

An **AI Explanation** tab in the workbook, the same text as section 14 of the job report and the covering e-mail. It sums every material block and every labour row against the Estimate sheet's totals and states any difference in pounds and in a direction. Labour is split into set-up and run, with what it does at 1, 10, 25, 50, 100 and 250 off. The lines that still need a person are listed worst-first with the code, the money at stake and the drawing page — not counted.

Why it matters. "3 lines carry no price" is true and unactionable. This is what an estimator needs to finish the sheet in minutes rather than an afternoon.

One record behind every deliverable, and a report an estimator works from

NEW • 7 SEP

The Harrods run showed the last inconsistency: the workbook tabs, the covering e-mail, the job report and the quote each described the same estimate in their own words, and on three lines they disagreed — a configured plating rate called an "AI market indication", two totals for one figure, a tube leg priced on one length and reported on another. Fixed at the root over the weekend: **one costed record is built after the sheet calculates, and every document reads it.** Money, sources, gaps, decisions, finish and release status are now the same on all four, and a test renders all four from one job and checks them fact by fact.

The job report is rebuilt as **the estimator's page**: the unit cost and release status, then **the decisions still open** — issue, part, current assumption, action, owner and the money riding on each — then the bill of materials under its assemblies and the priced route. The drawing audit and the engine's diagnostics are still there, collapsed beneath. On 7332-01 that reads: packaging and delivery unpriced, plating scope on the frame, the transcribed leg length, two house rates to verify.

Job 7332 — 7332-01

Estimator's working copy — decisions first, the evidence behind them below

Job 7332-01 Drawing pack 10 pages · 1 PDFs · 6 DXFs matched Quantity basis 6 of

Summary

UNIT COST £80.09 per unit, ex VAT	MATERIAL £40.89 sheet, section, bought-in, commercial	LABOUR £33.59 per department row	QUANTITY 6 order quantity the sheet was priced at
---	---	--	---

NOT FOR RELEASE — 4 INPUTS OUTSTANDING

- 2 line(s) carry no price: PACKAGING, DELIVERY
 - 2 manufacturing decision(s) open
-
- 12 lines on the bill of materials, 9 carrying money on the sheet.
 - 2 **unpriced**, held at £0: PACKAGING, DELIVERY. The unit cost is understated by whatever they are worth.
 - 2 **on an SDI house rate marked INDICATIVE** (£16.63) — configured, reproducible, to verify: 7332-01-101-PLATE, P/P.
 - Finish charged: **Diamond polished and plated**.
 - Plating £15.83 is priced on **7332-01-008**; excluded because their own detail states another finish: 7332-01-001, 7332-01-002, 7332-01-003, 7332-01-004, 7332-01-005.

Figures are the Estimate sheet's own calculated cells.

Decisions required

6 items, worst first. Until these are answered the estimate is a draft and the quote says so.

#	Kind	Issue	Part	Current assumption	Action required	Owner	£ at stake
1	MISSING PRICE	PACKAGING carries no price	PACKAGING	held at £0 — the unit cost is understated by whatever it is worth	enter the per-unit figure	estimator	—
2	MISSING PRICE	DELIVERY carries no price	DELIVERY	held at £0 — the unit cost is understated by whatever it is worth	enter the per-unit figure	estimator	—
3	MANUFACTURING DECISION	Which members of 7332-01-101 are plated after welding	7332-01-101	mass priced on 7332-01-008; excluded because their own detail states another	confirm the plated member list and the process	estimator	£15.83

Sample: the first screen of the job report for the Harrods stand — what a unit costs, whether it can go out, and the six calls that decide it.

The workbook is five tabs, not nine NEW · 7 SEP

The estimators' own three (Estimate, Labour, Material Price Break) untouched, then two of ours instead of six. **AI Explanation** is the estimator's tab and now leads with the decisions. **AI Provenance** is the evidence: for every line the value used, its source, the evidence as a word (measured, transcribed, inferred), the charged money with the engine's own figure beside it as not charged, and the estimator's action; then the bill of materials under its assemblies, the route decision by decision including what was ruled out and why, and a block on **identity through the pack** — names that changed between drawings, lines costed with no drawing, drawing files that matched no part. Four tabs that carried the engine's pre-calculation figures beside the sheet's charged ones are gone.

Why it matters. It is the view onto what the extraction and the pricing did — which drawing, which reader, which rate — written for the estimator first and for us to diagnose a run second.

Parity, from the portal, on every run REBUILT

The parity harness had run once, in July. It was measuring the wrong things in five ways at once. Rebuilt: both workbooks are read by the one block reader, each side is reconciled to its own totals before anything is compared, differences are signed both ways, and the inputs behind a money gap — blank, gauge, quantity, nest — are reported with it. It runs from the estimating page whenever a manual sheet is attached, and files a ledger row per job.

One estimate, every quantity asked for NEW

"1, 50, 100, 250 and 500 is the norm now." The estimate runs once at the first quantity and the workbook is recalculated at each of the others, one file per quantity, with the order-level freight divided correctly rather than a pallet landed on each of 500 units.

A run is measured, not guessed at DONE

Every phase of a run is timed and printed slowest-first, and a machine profile samples memory and CPU during a live estimate. Those measurements — 38 GB peak, about four threads, roughly forty minutes a job — are the figures the workstation in section 05 is sized from.

This week's first job is through pre-flight IN PROGRESS

7332-01, a plated A3 signage stand for Harrods, exercised three things the earlier jobs had not: a subcontract plating line on a welded assembly, a bent square-tube leg, and a felt pad with no part code. All three now price and say where the figure came from. A ten-second pre-flight tool proves the route and the leg's length before the forty-minute run is spent. Reviewable, not yet releasable — plating membership and the tube length are Tim's calls, and the sheet says so.

After the parallel run — the automated pipeline, and on demand

The parallel run is what we are on now. Once we are through it, the engine stops being something a developer starts and becomes **a button an estimator presses**. The parts exist today as separate controls on the estimating page; the next step joins them into one run, and keeps each available on its own.

One button imports the full and latest drawing pack NEXT

Document Manager walks the project's SolidWorks references and stages the current pack — latest revision chosen by the data inside the file, not the filename — so the estimate is built from what design has now, not from whatever was copied into a folder.

One click generates the estimate, with the explains, and e-mails it with the quote NEXT

The workbook on the estimators' template, the estimator's page, the covering e-mail and the customer quote, from one run, sent to the people who asked for it. The quote carries a visible draft status until the open decisions are made, and the e-mail is the same words as the report.

Parity at the time of the run, or added afterwards PARTLY IN

Where a manual sheet exists it is attached and the AI-against-manual comparison runs with the estimate. Where the AI run happens first, the comparison is added when the manual sheet arrives — the same block-by-block report either way, filing a ledger row per job.

Amend the estimate, then generate the quote IN NOW

An estimator changes a rate or a line on the sheet and the customer quote is regenerated from their figure — no engine re-run, no drawing re-read, the amended sheet filed as the override record.

Print the pack from the portal IN NOW

A print button for the PDFs and DXFs of a drawing pack, run by the estimator from the SDI Intelligence portal against the pack the estimate was built from.

Beyond that — no timetable yet

China quotations. The buttons are in the portal; the analytics behind them are not yet built.

Multi-PDF packs. Working, and needs testing: a pack of many PDFs can be run against our model, or purely against an LLM for comparison.

03 Workstream 2 — SDI
Technical Design Intelligence

STATUS		OWNER	RESOURCE	NEXT GO-LIVE
P1 · 60% P2 · 90%		Y. Kumar	Sole developer	15 SEPTEMBER 2026 P2 follows on 29 Sep

Two threads. The **Document Manager tools** read SolidWorks project data without a SolidWorks seat and pull the right drawing pack into the estimating app (P1) and the shop-floor Production folder (P2). Then an **SDI in-house PDM** in four phases. Not an integration with the SOLIDWORKS PDM vault; SDI is building its own, on GitLab and LFS.

The week of 4 September

P2 demoed at the technical design meeting and approved APPROVED

Demoed to Ian B and Ed Cooper on 2 September. Approved, and the tool's name confirmed as **Production Design Extraction**. Actions captured: larger fonts, file-type filters, an extraction log, e-mail-notification options, and the OneDrive shared-drive file question. Revision handling is to be based on file names.

P2 at 90%, with a UI for user testing on 8 September

IN PROGRESS

- **Primary and supplementary assembly roles** — an independent file such as AC0706 is restored without creating a spurious BOM; only primary assemblies generate Excel BOMs and route their IGES to 3D CAD.
- **DWG / PDF revision-mismatch rule** with severity-based alerts rather than a blanket drop: high when the PDF is behind, medium when the SLDDRW disagrees, low when the DWG is behind. Surveyed 297 Boots projects to gauge frequency: 436 matched pairs, 34 split.
- **The OneDrive / toolbox "file missing" problem solved** — components on a designer's machine resolve by filename from configured read-only roots. Verified live: 980 filenames indexed, 10 of the 11 missing 11650 parts resolving.
- **Audit log** (who, what, duration per run), a **drive-health chip**, a Step 5 **shop-floor e-mail** that drafts from the run — dry-run by default, recipients locked server-side — and file-type filters on both review panes.
- **Slow scans diagnosed**: drives at 47–53 ms per file against a 2 ms baseline over Wi-Fi. A two-tier progress indicator added; the cause is under investigation and is one of the reasons the workstation sits on the same LAN as the file server.

Two days late on development, absorbed by P1's UAT preparation and the extra requirements from the design meeting. The P2 go-live moves with the re-plan below, not with these two days.

P3 Design Vault feasibility complete

DONE

Hardware, software and Dev / UAT / Prod environment analysis finished and e-mailed ahead of kick-off, so any blocker surfaces before the proof of concept starts. Git LFS holds every version of every binary; the strategy archives older versions once a job is final, and a returning project re-clones with "Pack and Go".

The plan, re-based on 4 September

REF	PHASE	WHAT IT GIVES YOU	WAS	NOW	STATUS
P1	Design files extraction Document Manager API	The correct drawing pack for a job straight into the estimating app. Serving it since 24 August; James is the user tester to 10 September.	15 Sep	15 Sep 26	60%

REF	PHASE	WHAT IT GIVES YOU	WAS	NOW	STATUS
P2	Production Design Extraction Document Manager API	Collects the shop-floor drawing pack on its own, with a why-not-copied report. User testing 11–24 Sep.	24 Sep	29 Sep 26	90%
P3.1	PDM — trustworthy files In-house, phase 1	Check-in and check-out, versioning, locking and history.	29 Oct	6 Nov 26	NOT STARTED
P3.2	PDM — CAD-aware In-house, phase 2	Where-used, missing references, version consistency, released-reference checks.	18 Nov	30 Nov 26	NOT STARTED
P3.3	PDM — engineering revisions In-house, phase 3	Approval workflow: WIP → pending approval → released, not approved, obsolete.	5 Jan	19 Jan 27	NOT STARTED
P3.4	PDM — release workflows In-house, phase 4	Separate release routes for WIP, prototype and production components.	14 Jan	1 Feb 27	NOT STARTED

Why the dates moved, and why that is the honest version

The 27 August dates assumed each tool's deployment took no developer time. It does: deployment and go-live are hands-on days, and with one developer they have to be carved out of the next tool's build. The tracker now slots them in explicitly — two days for P2, two to three for each PDM phase — and the plan reports no clashes. Leave from 10 December to 4 January is unchanged and is what pushes P3.3 and P3.4 into the new year.

The lever is still a second pair of hands. Every date from P3.1 onwards depends on one person being available.

Watch-points, in Yogesh's words

- **The Design Vault proof of concept needs a Linux / GitLab machine by 10 September.**
That is the shared workstation in section 05. If it is not ready, he switches to the design-generation work (PDF / DXF / IGES) scheduled later, so nothing stalls.
- **Once the Vault is live the W: drive stops being the single source of truth.** Proposed: sync W: on released status. Raised at the daily AI meeting on 3 September with the need for backups and proper Dev / UAT / Prod environments.
- **Network scan speed over Wi-Fi is too slow** — under investigation, and answered structurally by putting the workstation beside the file server.

04 Workstream 3 — SDI
Creative Design Intelligence

STATUS

OWNER

PROJECTS

UAT from 7 Sep

M. Yazir

1 in UAT · 1 on hold · 1 paused

FIRST GO-LIVE

~25 SEPTEMBER 2026

still the earliest in the programme

SERVICE NAME	TRACKER NAME	FOR	POSITION	LIVE	DONE
SDI Drawing Search Intelligence	Fixture Library	Ed, Stuart	UAT FROM 7 SEP	~25 Sep 26	50%
SDI Client Briefing Intelligence	Client Briefing	Stuart, Bec	ON HOLD · 4 SEP	—	25%
Image Upscaler	Image Upscaler	Sarah, Dean	PAUSED AUG 26	—	56%

Drawing Search goes into UAT this week 7 SEP

Studio designers start testing on real projects from Monday 7 September, against the round-2 build that is still indexing the remaining images and being hardened to 15 September. The tool and its user guide are on the SDI Intelligence portal — the service page describes what it is and where it stands, and the guide, written by Muhammad, shows the three ways to search and what a result card carries.

Read the dates together. UAT runs to 25 September, integration testing round 2 runs 15–20 September inside it, and go-live is the day UAT ends. Anything found in the final week lands on the rollout date directly. Unchanged from 27 August, and still the single most likely place for the programme's first go-live to slip.

Client Briefing is on hold, and changes shape DECISION · 4 SEP

Requirements gathering with Stuart stops at 25%. The project is not cancelled: **James Gray and Yogesh Kumar pick it up as a set of AI real-time agents** rather than as a single application, which is a different build from the one the tracker priced — and the code review and architecture work tasked to MJ at the 3 September meeting is the first step of it. A plan follows. Stuart and Bec's approved proof of concept stands as the statement of what it has to do.

Muhammad moves to the manufacturing workstream CHANGE

Business analysis, user stories and documentation for the **Manufacturing / CNC SDI Intelligence** automations — the workstream that closes the loop from estimate to shop floor and has, until now, had no tracker and no dates. The first job on it is now specific: **map the live production spreadsheet for BOMs and routes for the warehouse**, so that process can be automated and is understood on the way into **Sage X3**; **map the design DXF process onto CNC machining**; and document both as a **BRD and user stories**, planned and executed with James Gray. Client Briefing is written up to an extent before it is parked. He keeps Drawing Search through UAT and go-live.

SDI Drawing Search Intelligence · phase detail

#	PHASE	START	END	DURATION	STATUS	NOTES
01	Proof of concept Stakeholder validation	1 Jul 26	1 Jul 26	1 day	DONE	Protot demo & Stud Green receiv
02	Development — round 1 Full build	2 Jul 26	31 Jul 26	4 weeks	DONE	CLIP s PDF in GPU s Flask cache
03	Unit testing Internal — developer	1 Aug 26	2 Aug 26	2 days	DONE	Searc accur edge c GPU f netwo safety
04	Integration testing — round 1 Live data test	3 Aug 26	7 Aug 26	5 days	DONE	Findir Rende folders indexe (~162 ~268k back t
05	Development — round 2 Fixes & hardening	1 Sep 26	15 Sep 26	2 weeks	IN PROGRESS	Indexi ~446k remain image rules, review guide publis

#	PHASE	START	END	DURATION	STATUS	NOTES
06	Integration testing — round 2 Re-test after fixes	15 Sep 26	20 Sep 26	5 days	PENDING	Verify ~268k search Confir model accur
07	UAT User acceptance testing	7 Sep 26	25 Sep 26	3 weeks	STARTS THIS WEEK	Studic design on rea projec Feedt sign-o
08	Go live Studio-wide rollout	~25 Sep 26	—	—	PENDING	IIS/ng deploy auther index K: driv

Image Upscaler

PAUSED AUG 26 · 56%

Unchanged. Paused on studio priorities, not on any failure; the CMYK conversion it produced remains in daily use. Restartable when capacity allows.

05

The shared workstation

One machine, three workloads, two operating systems. Every figure in the request is measured from what is already running, not taken from a datasheet.

REQUEST	BUDGET	SUPPLIER	NEEDED BY
1 × workstation	£4,800–5,050 ex-VAT	Scan 3XS	10 SEPTEMBER 2026 purchase this week

Estimating engine · J. Gray

Running manually on a laptop today. Needs 38 GB and the fastest single core available: SolidWorks and Excel are single-threaded, and it drives both through an interactive Windows desktop.

Drawing Search · M. Yazir

Must be always-on and beside the file server. A 16 GB SolidWorks-certified GPU takes an image search from 9.5 s to 1.1 s; over VPN, indexing takes days rather than hours.

Design Vault POC · Y. Kumar

Two Ubuntu guests for GitLab and PostgreSQL under Hyper-V, with a Windows Server guest later. Starts 10 September.

The shape, in one line each

- **CPU** — AMD Ryzen 9 9950X: the fastest single core, not the most cores.
- **Memory** — 128 GB as 2×64 GB ECC, two slots free to reach 256 GB. Measured need is 106–114 GB across the three.
- **GPU** — 16 GB SolidWorks-certified card; the one line Muhammad's requirement turns on.
- **Always-on** — mirrored NVMe system disks, a 4 TB data disk for the Git LFS volume, and a UPS, because it runs unattended overnight for three teams.
- **Windows 11 Pro on the metal**, Ubuntu as Hyper-V guests. Not Windows Server, because SolidWorks is unsupported on it.

Two decisions needed before the order goes

1. Can it sit on the same LAN as sdi-dc01? IT. Free, and the single most important line in the request. Over VPN the file server is 226 ms away and indexing crawls; on the same network the same job takes hours. It cannot be fixed later by buying more machine.

2. Is AD integration for Drawing Search firm, or nice-to-have? Muhammad. SolidWorks cannot run on Windows Server, so the search would run under Windows 11 Pro without AD group control. If AD is a hard requirement the host OS choice reopens.

Not in this budget, flagged for later: a 256 GB memory upgrade (~£500) when the Phase 4 Windows worker arrives, and a Windows Server licence, CALs and a second SolidWorks seat at the same point. Supersedes the single-purpose server of 25 August, which sized for one workload rather than three.

06 Open across the programme

Ordered by what it costs to leave alone. Items carried from 27 August keep their wording where nothing has changed; items closed since are listed last, so a reader can see the list shrink as well as grow.

Four estimates awaiting review ACT

11762-17, 11762-02, 11908-21 and 12552 are with Dave's team. Five more go out this week. The go-live target is measured on what comes back, and the one review returned so far turned into three fixes in a day.

Workstream 1. Ask: five back for five out, from this week.

Two decisions on the workstation, then the order ACT

Same-LAN placement beside sdi-dc01 (IT) and whether AD integration is firm (Muhammad). Needed by 10 September for the Design Vault proof of concept; if it is late, Yogesh switches work rather than waits.

All three workstreams.

Packaging and delivery are held at £0 OPEN

By decision. The market indication that filled them moved between runs and was 18% of a unit on 12552. The lines stay on every sheet at zero with a named owner until the estimators provide their own calculation; the engine then carries it as a house rate.

Workstream 1. Needs a figure from estimating, not from engineering.

Supplier price lists are still not loaded OPEN

The ingester is built and tested. It needs the actual files: Elite, Eagle and Thermaset. Every catalogue loaded removes estimator inputs permanently and replaces indicative figures with reproducible ones.

Workstream 1. Carried from 27 August, unchanged.

Three rates on 7332-01 are labelled INDICATIVE and wait on Tim OPEN

Zinc plating at £2.50/kg with a £95 minimum, section tube at £7.29/kg, and a 20p felt pad. Each is on the sheet, named as indicative, with the reason. Which parts of the weldment are plated is an estimator's call and the plate line says so.

Workstream 1. Labelled holds, never a silent zero.

Client Briefing needs its new plan NEW

On hold from 4 September and to be picked up as AI real-time agents by James Gray and Yogesh Kumar. Until the plan is written the ~Nov 2026 date has no basis and is withdrawn.

Workstream 3.

The manufacturing workstream gets its first written record NEW

Muhammad's business analysis for the Manufacturing / CNC automations: the live production spreadsheet for BOMs and routes mapped for the warehouse and for Sage X3, the design DXF process mapped onto CNC machining, both written up as a BRD and user stories, planned and executed with James Gray. No dates are claimed until that record exists.

Workstream 4, planned.

The W: drive stops being the single source of truth when the Vault goes live NEW

Raised by Yogesh at the 3 September meeting, with the need for backups and proper Dev / UAT / Prod environments. Proposed: sync W: on released status. A design decision for P3.1, which starts 11 September.

Workstream 2.

Drawing Search go-live has no buffer OPEN

Studio-wide rollout on 25 September is the same day UAT ends. Unchanged, and now the UAT is real: designers start on 7 September against a build that hardens to the 15th.

Workstream 3. A decision for the owner, not a fix.

Workstream 2 has one developer and no cover OPEN

Now visible in the dates rather than beside them: the re-plan carved deployment days out of the next build because there is nobody else to give them to. Every date from P3.1 onwards depends on one person, and leave from 10 December to 4 January sits inside them.

Workstream 2. Cannot be recovered by re-planning.

Carried, with no change reported CARRIED

- **The BrightHR client secret has never been rotated** — still the only cure for a value that sat in a public repository's history.
 - **SDI-APP01** still needs the rotated database password and the configuration script that tells the health check which build it is running.
 - **Two price sources wired to empty tables** — rung 3 of the price chain reads a migrated catalogue whose rows were left inactive.
 - **Size is not weighted in description matching** — recorded as a deliberately failing test.
 - **The PDM requirement register is still open** at around 50 items.
 - **Which machines get a SolidWorks seat** beyond the estimating laptop.
-

Workstreams 1 and 2. Listed so they are not rediscovered; none moved this period.

Closed since 27 August

CLOSED

- **DWG drawings are no longer silently ignored** — a DWG in a pack is converted by whichever converter the machine has, and the run says which.
- **A category word is no longer used as a part code**, and a bought-in with no code prices from a labelled standard-commodity rate rather than shipping at £0.
- **The parity report measures the estimate**, not its own parser, and runs from the portal on every job with a manual sheet attached.
- **The server is specified from measurement** — the 25 August single-purpose server is superseded by the shared workstation in section 05.

SDI PROGRAMME STATUS · COMBINED REPORT · ISSUE 2 · ISSUED 7 SEPTEMBER 2026 · SUPERSEDES 27 AUGUST 2026

SOURCES · SDI INTELLIGENCE COMMIT HISTORY 30 AUG – 7 SEP · YOGESH KUMAR STATUS 4 SEP AND PROJECT PLAN TRACKER WEEK 04 SEP · ALL PROJECTS DELIVERY TRACKER · SHARED WORKSTATION CAPITAL REQUEST 3 SEP ESTIMATING GO-LIVE TARGET · SEPTEMBER / OCTOBER 2026 – DECIDED ON REVIEWS RETURNED FROM THE PARALLEL RUN

SDI DISPLAYS · LOUGHBOROUGH · WE.ARE.SDI
